

FRANNA MAC25-SL 25T Pick and Carry Compliance Pack



METCALF
CRANE SERVICES

www.metcalfcranes.com.au

78 - 82 Freight Drive Somerton Vic 3062

Phone: (03) 9308 0044

Email: sales@metcalfcranes.com.au

Compliance Pack

TABLE OF CONTENTS

Table of Contents.....	2
Version Control.....	3
Introduction.....	4
Purpose	4
General Information.....	4
Operator's Manual	5
Plant Log Book-Daily Inspection.....	6
Registration of Plant.....	6
Maintenance Inspections and Green Sticker program	7
Plant Risk Assessment	8
Lifting Gear Register	9
Wire Rope, Winch and Hook Certificates.....	11
Insurance Plant and Equipment	13
Insurance Public and Products	14
Insurance WorkCover	15
Enterprise Bargaining Agreement.....	16

Compliance Pack

VERSION CONTROL

Version	Date	Author	Remarks
Version 1.0	March 2018	Safety Manager	New document

REVISION HISTORY

Revision	Date	Description
Version 1.1	June 2018	Updating Lifting Register & EBA & Insurances
Version 1.2	Oct 2018	Update lifting register
Version 1.3	Jan 2019	Update lifting register & Plant risk assessment
Version 1.4	Mar 2019	Updating green sticker
Version 1.5	Apr 2019	Update lifting gear register
Version 1.6	May 2019	Adding wire rope, winch and hook certs
Version 1.7	July 2019	Updating lifting gear register & insurance certs
Version 1.8	Oct 2019	Updating lifting gear register
Version 1.9	Jan 2020	Updating lifting gear register & plant risk assessment
Version 2.0	March 2020	Updating green sticker and lifting gear register
Version 2.1	July 2020	Updated lifting gear register and insurance certificates
Version 2.2	Oct 2020	Updated lifting gear register
Version 2.3	Dec 2020	Updating lifting gear register and Plant risk assessment

Compliance Pack

INTRODUCTION

Metcalf Crane Services recognises the importance of ensuring that all the correct information is outlined to you as our clients.

This document provides you with the relevant information to ensure that Metcalf Crane Services have the correct documentation for the crane that you wish to engage to provide you with the equipment and services that to desire.

PURPOSE

The purpose of this Compliance pack is to provide you with the right documentation and or information to assist you with making the right decision that Metcalf Crane Services have the right equipment and documentation required to complete the operation for you.

GENERAL INFORMATION

Make	Franna
Model	MAC25-SL
Serial Number	251149
Registration	1MN 6UB (unit 83)

Compliance Pack

OPERATOR'S MANUAL

The Operator's Manual can be found within the cabin of the crane for easy reference when required.

The Metcalf office also has access to an electronic copy of the Operator's Manual. The cover of this manual is seen in Figure 1.

Figure 1

ABN : 88 010 671 048
ACN : 010 671 048
E-MAIL : info@terex.com.au
Internet : www.terex.com.au



Terex Lifting Australia Pty. Ltd.



RATED CAPACITY MANUAL

MODEL MAC 25

16.6t REAR AXLE WEIGHT
BOOK PART NUMBER MXC1347B

HYDRAULIC ALL TERRAIN PICK & CARRY CRANE "SUPERLIFT"

25 TONNE MAXIMUM RATED CAPACITY



**Do not operate this crane unless you have read and
understood the information in this book.**

Compliance Pack

PLANT LOGBOOK - DAILY INSPECTION

The Use of the Plant logbook is completed by the crew prior to commencing work each day/shift.

This is the responsibility of the Operator to ensure this is done. See Figures 2 and 3 for a copy of the cover page and example of the Daily inspection logbook form

Figure 2




Figure 3

PLANT AND EQUIPMENT <small>ON A LOG BOOK FOR CRANE OPERATIONS</small> <small>with a valid license</small>		OWNER NAME:		DATE/FA: 9002																		
		PROJECT NO:		DATE/FA: _____																		
OPERATIONS DAILY AND WEEKLY CHECKLIST <small>FOR EVALUATION AND TO IDENTIFY VARIATIONS FOR USE OF LOG BOOK</small>		SITE NO:		DATE/FA: _____																		
		SUBSIDIARY:		DATE/FA: _____																		
		CRANE NO.	CRANE SERIAL NO.	CRANE TYPE	THURSDAY	FRIDAY	SATURDAY	SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY	SUNDAY	MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY	SUNDAY
1. CRANE IDENTIFICATION																						
2. CRANE CONDITION																						
3. CRANE LOADS																						
4. CRANE LOADS																						
5. CRANE LOADS																						
6. CRANE LOADS																						
7. CRANE LOADS																						
8. CRANE LOADS																						
9. CRANE LOADS																						
10. CRANE LOADS																						
11. CRANE LOADS																						
12. CRANE LOADS																						
13. CRANE LOADS																						
14. CRANE LOADS																						
15. CRANE LOADS																						
16. CRANE LOADS																						
17. CRANE LOADS																						
18. CRANE LOADS																						
19. CRANE LOADS																						
20. CRANE LOADS																						
21. CRANE LOADS																						
22. CRANE LOADS																						
23. CRANE LOADS																						
24. CRANE LOADS																						
25. CRANE LOADS																						
26. CRANE LOADS																						
27. CRANE LOADS																						
28. CRANE LOADS																						
29. CRANE LOADS																						
30. CRANE LOADS																						
31. CRANE LOADS																						
32. CRANE LOADS																						
33. CRANE LOADS																						
34. CRANE LOADS																						

REGISTRATION OF PLANT

The Occupational Health and Safety Amendment Regulations 2014 came into effect on 1 July 2014. From 1 July you no longer required to register items of plant with the WorkSafe or re-register plant every five years.

With advances in technology, the WorkSafe is able to rely on other sources, including an extensive network of stakeholders and supplier, for information about the location of plant in Victoria, and so the registration of plant isn't as important as it once was.

Some sources that can be used to track plant equipment are VicRoads registration and the CraneSafe program (Section 8).

If Metcalf still have the crane registered with as plant through WorkSafe a copy will be here. (Figure 4)

Figure 4 NA

Compliance Pack

MAINTENANCE INSPECTIONS AND GREEN STICKER PROGRAM

These inspections are carried out by our qualified Mechanic at approximately every 250hrs; these records are stored at the office and are available on request

The mobile crane industry initiated a voluntary crane assessment program throughout Australia. Developed in consultation with the mobile crane industry as a whole, the program aims to augment existing safety standards with annual assessments of mobile cranes now being made by CraneSafe (a division of The Crane Industry Council of Australia).


The program will provide crane owners, suppliers and users in Australia with a common industry wide system for third party assessment of the safety aspects of their cranes. The CraneSafe assessment program is voluntary and while it does not form part of any legislation or regulatory scheme, it will assist crane owners and users in Australia to meet their obligation under the OH&S (plant) regulations to ensure that their cranes are in a safe condition. The program provides crane owners and operators with a process for third party assessment of the safety aspects of their cranes that complies with the regulations of Parts 1, 3, 4, 5, 11, 19 and 20 of AS2550 for annual inspection.

All Metcalf Cranes are involved in this program and a copy of the Green sticker is provided as evidence of this. (Figure 5)

Major inspections should generally be undertaken when the crane, hoist or winch has reached the end of its design life. If the design life is unknown, in most cases, the major inspection of mechanical components should be undertaken after a maximum of 10 years of service.

This report will be attached in figure 6; NA will be added here if the Crane is less than 10 years old.

Figure 5

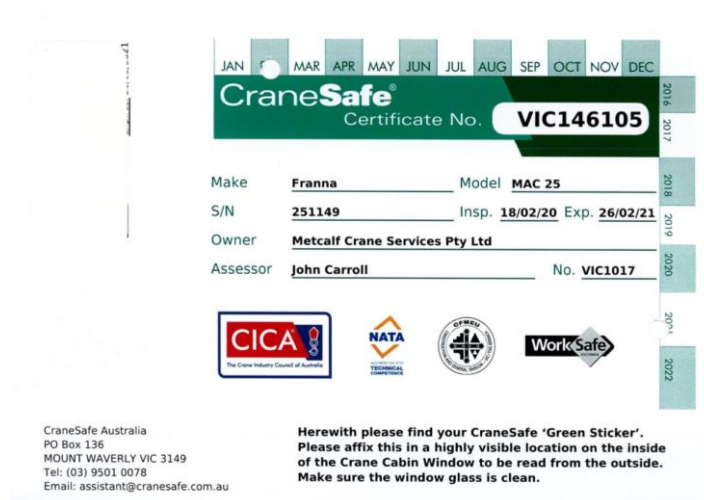

CraneSafe Certificate No. **VIC146105**

Make **Franna** Model **MAC 25**

S/N **251149** Insp. **18/02/20** Exp. **26/02/21**

Owner **Metcalf Crane Services Pty Ltd**

Assessor **John Carroll** No. **VIC1017**

CICA **NATA** **WorkSafe**

CraneSafe Australia
PO Box 136
MOUNT WAVERLY VIC 3149
Tel: (03) 9501 0078
Email: assistant@cranesafe.com.au

Herewith please find your CraneSafe 'Green Sticker'.
Please affix this in a highly visible location on the inside
of the Crane Cabin Window to be read from the outside.
Make sure the window glass is clean.

Figure 6 NA

Compliance Pack

PLANT RISK ASSESSMENT

The review of the manufactures Risk assessment takes place when the plant is been purchased by the company, if the manufacture has not supplied one, Metcalf will provide one.

The RA will be reviewed periodically and in the event of a serious incident.

This RA can be found in the crane cabin. (Figure 7)

Figure 7

RISK ASSESSMENT					
ISSUE DATE: 01 January 2021			DATE OF REASSESSMENT: 31 December 2021		
CRANE SAFE SERIAL NUMBER: VIC146105			CRANE SERIAL NUMBER: 251149		
CONDUCTED BY: B. Schiopu					
Item#	Hazard	Is there a risk? (Y/N)	Control Measures	Are the control measures practicable? (Y/N)	Date of Implementation
Various Set Up Configurations					
1.	General assembly: Lifting equipment failure / personal injury, cranes overturning, poor rigging method	Y	Lead rigger to have continual communication with BOTH crane operators when lifting crane components. Lifting equipment to be tagged and tested, visual check conducted before each use. Non-serviceable items to be removed immediately. SWL of lift gear is fit for task and lifts. Visual inspection of lifting points when connecting rigging equipment, if lifting points are in poor condition or damaged report immediately Gloves to be worn while using lifting equipment. Weather to be monitored. Exclusion zones established. Lift only from approved crane pads Riggers to maintain clear communication with crane operator when connecting rigging gear. Riggers to keep hands clear of pinch points when attaching rigging equipment. Complete a second check of rigging method prior to lifting components.	Y	Prior to use by the hirer. Prior to supply.

Compliance Pack

LIFTING GEAR REGISTER

The Lifting Register is maintained by Metcalf for all their lifting equipment which is a live document that can and will change on a regular basis. All lifting equipment which includes but not limited to Slings, chains and shackles will be tested to Australian Standards. This crane's lifting register is below (Figure 8)

Figure 8

PLANT / EQUIPMENT LIFTING REGISTER - U83 Franna MAC25-SL										
Last Updated 21/12/2020 @ 8:23am										
ID / Serial Number	Certificate Number	Description	Length (M)	W.L.L	External Annual Inspection Date	Next External Inspection Date	P/F	Internal R/G/B/Y Inspection Date	Internal R/G/B/Y Expiry Date	RGBY Colour
R1217/3X4/06144	JIC-409035	3t x 4m Roundsling	4 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R1217/3X4/06150	JIC-409036	3t x 4m Roundsling	4 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
FS16130-51-006	JIC-409034	1t x 1m Flat Webbing Sling	1 Mtr	1T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R1712-48066	JIC-409042	4t x 3m Roundsling	3M	4T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.1	JIC-408994	12T Bow Shackle		12T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.2	JIC-408995	12T Bow Shackle		12T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.3	JIC-408996	12T Bow Shackle		12T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.4	JIC-408997	12T Bow Shackle		12T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.5	JIC-408998	8.5T Bow Shackle		8.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.6	JIC-408999	8.5T Bow Shackle		8.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.7	JIC-409000	8.5T Bow Shackle		8.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
1708.8	JIC-409001	8.5T Bow Shackle		8.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R17079-20112	JIC-409038	4t x 4m Roundsling	4 Mtr	4T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
F14010-4176	JIC-409047	2T x 2m Flat Webbing Sling	2 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
F14010-4191	JIC-409049	2T x 2m Flat Webbing Sling	2 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
F14010-4387	JIC-409048	2T x 2m Flat Webbing Sling	2 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
FM030618190	JIC-409050	2T x 2m Flat Webbing Sling	2 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
KBW.1	JIC-409003	12.5T Container Hook		12.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS10	JIC-409007	3.2t Bow Shackle		3.2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS11	JIC-409008	3.2t Bow Shackle		3.2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS12	JIC-409009	3.2t Bow Shackle		3.2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS13	JIC-409010	3.2t Bow Shackle		3.2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS14	JIC-409011	2t Bow Shackle		2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS15	JIC-409012	2t Bow Shackle		2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS16	JIC-409013	2t Bow Shackle		2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS17	JIC-409014	2t Bow Shackle		2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS2	JIC-409015	6.5t Bow Shackle		6.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS3	JIC-409016	6.5t Bow Shackle		6.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
MS4	JIC-409017	6.5t Bow Shackle		6.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red

Compliance Pack

MS5	JIC-409018	6.5t Bow Shackle		6.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
NCAR1	JIC-409004	12.5T Container Hook		12.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
PBVL1	JIC-409005	12.5T Container Hook		12.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
PVVR1	JIC-409006	12.5T Container Hook		12.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R17079-20152	JIC-409037	4t x 4m Roundsling	4 Mtr	4T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R17125-8082	JIC-409041	4t x 3m Roundsling	3 Mtr	4T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.1	JIC-409020	10mm x 5.3m x 2 Leg G80 Chainsling complete with shorteners self locking hooks	5.3 Mtr	5.5T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.2	JIC-409021	10mm x 5.3m x 2 Leg G80 Chainsling complete with shorteners self locking hooks	5.3 Mtr	5.5T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.3	JIC-409024	13mm x 5.3m x 2 Leg G80 Chainsling complete with shorteners and self locking hooks	5.3 Mtr	9.2T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.4	JIC-409025	13mm x 5.3m x 2 Leg G80 Chainsling complete with shorteners and self locking hooks	5.3 Mtr	9.2T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.5	JIC-409026	13mm x 2.4mm x 2 Leg G80 Chainsling complete with shorteners and self locking hooks	2.4 Mtr	9.2T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.6	JIC-409022	10mm x 1.4m x 2 Leg G80 Chainsling complete with shorteners self locking hooks	1.4 Mtr	5.5T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.7	JIC-409023	10mm x 1.5m x 2 Leg G80 Chainsling complete with shorteners self locking hooks	1.5 Mtr	5.5T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
83.8	JIC-409027	16mm x 3.9m x 2 Leg G80 Chainsling complete with shorteners and self locking hooks	3.9 Mtr	13.8T @ 60 DEGREES	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
BN20	JIC-409002	8.5T Bow Shackle		8.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
BN54	JIC-409019	6.5t Bow Shackle		6.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
180818/150/122	JIC-409045	3t x 3m Roundsling	3 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
180818-96-093	JIC-409032	2t x 4m Roundsling	4 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
180818-84-013	JIC-409033	2t x 4m Flat Webbing Sling	4 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
74909-1833	JIC-409031	3t x 3m Roundsling	3 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
74909-1510	JIC-409030	3t x 3m Roundsling	3 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
110	JIC-408988	5t Clutch Lifter		5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
098	JIC-408983	2.5t Clutch Lifter		2.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
159	JIC-408985	1.3t Clutch Lifter		1.3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
155	JIC-408984	1.3t Clutch Lifter		1.3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
161	JIC-408986	1.3t Clutch Lifter		1.3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
164	JIC-408987	1.3t Clutch Lifter		1.3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
097	JIC-408982	2.5t Clutch Lifter		2.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
096	JIC-408980	2.5t Clutch Lifter		2.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
037	JIC-408989	5t Clutch Lifter		5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
005	JIC-408981	2.5t Clutch Lifter		2.5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
039	JIC-408990	5t Clutch Lifter		5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
040	JIC-408991	5t Clutch Lifter		5T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
043	JIC-408992	10t Clutch Lifter		10T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
044	JIC-408993	10t Clutch Lifter		10T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
F14134-20042	JIC-409028	4t x 4m Roundsling	4 Mtr	4T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
F15047-17068	JIC-409029	4t x 4m Flat Webbing Sling	4 Mtr	4T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R1217/2X1/03266	JIC-409039	2t x 1m Roundsling	1 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R1217/2X1/03260	JIC-409040	2t x 1m Roundsling	1 Mtr	2T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R18238/10619	JIC-409044	3t x 2m Roundsling	2 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R918/3X2/2375	JIC-409043	3t x 2m Roundsling	2 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red
R18196-15-253	JIC-409046	3t x 3m Roundsling	3 Mtr	3T	12-Mar-20	12-Mar-21	PASS	01-Jan-21	31-Mar-21	Red

Compliance Pack

WIRE ROPE, WINCH AND HOOK CERTIFICATES

JATCO ENGINEERING (VIC) P/L
11 Daveyduke Drive, Mitchell Park, Wendouree 3355
info@jatco.com.au ph: 03 5339 4765

WIRE ROPE INSPECTION & EXAMINATION

Machine: MAC 25/1A9 Application: MAIN HOIST

Type of rope: 4mm 35x7 Bunnell ☐ left hand lay ☒ right hand lay


Nominal diameter (mm): 14mm ☐ regular lay ☒ lang's lay

Tensile strength (N/mm²): 182.4 kN ☐ ungalvanized ☐ galvanized

Rope length (m): 110 type of end fitting: OPER FIBER

Date of installation: Jan 2018 working hours to date: 1697 Tonn

Location measured	no. of broken wires on 10 x d	abrasion	Corrosion	Diameter/Ø-reduction mm/%	Other
10	<u>NIL</u>	*	*	eff. Ø of new rope <u>14.27</u>	**
20	<u>NIL</u>	x	x	<u>14.25</u>	
30	<u>NIL</u>	x	x	<u>14.27</u>	
40	<u>NIL</u>	x	x	<u>14.26</u>	
50	<u>NIL</u>	x	x	<u>14.27</u>	
60	<u>NIL</u>	x	x	<u>14.28</u>	
70	<u>NIL</u>	x	x	<u>14.27</u>	
80	<u>NIL</u>	x	x	<u>14.20</u>	
90	<u>NIL</u>	x	x	<u>14.27</u>	

Final evaluation: AS NEW CONDITION SUITABLE FOR FURTHER USE date / signature: 25/2/2019 

* description, e.g. no. little, etc ** comments, e.g. description of a rope deformation

Compliance Pack


JATCO ENGINEERING (VIC) PTY LTD
PO. BOX 260, BALLARAT, VIC 3353
PH: 03 5339 4755 FAX: 03 5339 1677

CERTIFICATE OF INSPECTION AND TEST


Note: This record is to be kept on location with the relevant hook(s)


DESCRIPTION OF HOOK(S): <u>LOAD HOOK</u>		Crane No: <u>UNIT 83</u>
Manufacturer: <u>CROSBY</u>		
Type/Model: <u>FRANNA MAC 25 SN 251149</u>		
No Sheaves: <u>3</u>	Size Sheaves: <u>14</u>	
Tare Weight: <u>230 KG</u>		
IDENTIFICATION MARKINGS OR SERIAL NUMBERS:		
ID Numbers: <u>BBT 23234</u>		
WLL: <u>20,000 KA</u>		
Proof Load (Mechanical): <u>VISUAL</u>		
Additional Test Results Attached (Mechanical): YES / NO		
TYPE OF INSPECTION:		
Visual:	<input checked="" type="checkbox"/> YES	<input type="checkbox"/> NO
Mechanical:	<input type="checkbox"/> YES	<input type="checkbox"/> NO
Comments: <u>Y-4 INCH</u>		

Distance Measured Y, Y1, Y2

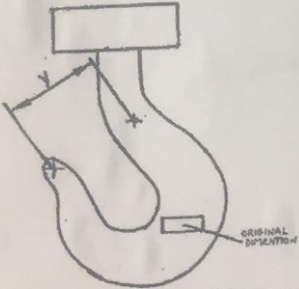

Y Y-4 INCH

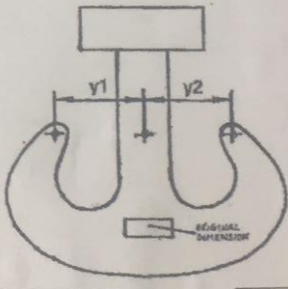




Additional Comments:

DECLARATION:

In accordance with AS2550.1, Section 8.2, this test certificate has been produced to indicate that a competent person has inspected the stated items.


Signature of Inspector: 

Name of Inspector: JOHN GARROD

Date of Inspection: 26-2-2019

INSURANCE PLANT AND EQUIPMENT

Figure 9



Underwriting Agencies of Australia Pty Ltd

AFSL: 238517 ABN: 86 003 565 302

Industrial Special Plant "ISP" Certificate of Currency
Section 1 – "Damage" + Section 6 – "Road Risk"
 This certificate acknowledges that the Policy referred to is in force for the period shown,
 the summary of cover is listed below.

Date:	Friday, 26 June 2020
Policy Number:	13TI031351ISP
Insured:	Metcalf Crane Services, Metcalf Heavy Haulage, Metcalf Investments Pty Ltd
Period of Insurance:	1 July 2020 to 1 July 2021 at 4:00pm Local Standard Time
Policy Wording:	QM2003-0819 Industrial Special Plant (ISP)
Insurer:	QBE Insurance (Australia) Limited

Policy Details:

Section 1 – "Damage"	
Total Sum Insured:	\$38,764,255
Excess:	as per Policy Schedule
Section 3 – "Additional Benefits"	
Cover Details:	as per Policy Schedule
Excess:	as per Policy Schedule
Section 6 – "Road Risk"	
Limit of Indemnity:	\$30,000,000
Excess:	as per Policy Schedule

Items Covered:

31 X CRANES (REG)	\$32,255,985
4 X CRANES (UNREG)	\$671,005
1 X FORKLIFT (UNREG)	\$20,000
1 X CRANE TRUCK (REG)	\$100,000
13 X TRUCKS (REG)	\$964,296
11 X PRIME MOVERS (REG)	\$1,820,161
25 X TRAILERS (REG)	\$1,602,917
3 X FUEL TANKS (UNREG)	\$187,174
REGISTERED HIRED IN PLANT	
19 X UTILITIES (REG)	\$859,438
3 X SEDANS / WAGONS (REG)	\$283,279

Subject at all times to the Terms, Conditions, Definitions, Exclusions & Endorsements of the Policy.


This certificate of currency was generated with compliments from:
 Brooklyn Hunter
 Phone: 03 9134 4400

Industrial Special Plant ("ISP") is underwritten by QBE Insurance Australia Limited ABN: 78 003 191 035 AFSL: 239545 of 2 Park Street, Sydney NSW 2000.
 Underwriting Agencies of Australia ("UAA") ABN: 86 003 565 302 AFSL: 238517 act as the agents of the Insurer.

Compliance Pack

INSURANCE PUBLIC AND PRODUCTS

Figure 10



Underwriting Agencies of Australia Pty Ltd
AFSL: 238517 ABN: 86 003 565 302

Industrial Special Plant "ISP" Certificate of Currency
Section 7 – "Broadform Liability"

This certificate acknowledges that the Policy referred to is in force for the period shown,
the summary of cover is listed below.

Date:	Friday, 26 June 2020
Policy Number:	13TI031351ISP
Insured:	Metcalf Crane Services, Metcalf Heavy Haulage, Metcalf Investments Pty Ltd
Period of Insurance:	1 July 2020 to 1 July 2021 at 4:00pm Local Standard Time
Policy Wording:	QM2003-0819 Industrial Special Plant (ISP)
Insurer:	QBE Insurance (Australia) Limited

Policy Details:

Section 7 – "Broadform Liability"

Insured's Business Activities: MOBILE CRANE OPERATIONS, WET & DRY HIRE, RIGGING & HEAVY HAULAGE TRANSPORT

Limit of Liability: \$30,000,000 (Public Liability) any one Occurrence; and
\$30,000,000 (Products Liability) any one Occurrence and in the Aggregate any one Period of Insurance.

Excess: as per Policy Schedule

This policy includes a Principals Indemnity provision; refer to Section 7.C Additional Benefits, 3.(e) "Cover for Others" of the Policy Wording for full details.

Noted as Principal: Nil

Subject at all times to the Terms, Conditions, Definitions, Exclusions & Endorsements of the Policy.


This certificate of currency was generated with compliments from:
Brooklyn Hunter
Phone: 03 9134 4400

Industrial Special Plant ("ISP") is underwritten by QBE Insurance Australia Limited ABN: 78 003 191 035 AFSL: 239545 of 2 Park Street, Sydney NSW 2000.
Underwriting Agencies of Australia ("UAA") ABN: 86 003 565 302 AFSL: 238517 act as the agents of the Insurer.

INSURANCE WORKCOVER

Figure 11

**CERTIFICATE
OF CURRENCY**



EML
Mutual since 1910
Authorised Agent of the Victorian WorkCover Authority

1. STATEMENT OF COVERAGE

This employer is registered for WorkCover Insurance to cover its liabilities under the *Workplace Injury Rehabilitation and Compensation Act 2013* (and amendments).

This Certificate is valid from: to:

The information provided in this Certificate of Currency is correct at:

2. EMPLOYER'S INFORMATION

WorkCover Employer Number:

Legal Name:

Trading Name:

ABN:

ACN/ARBN:



Chris Papadopoulos
Premium and Policy Manager
EML VIC Pty Ltd
For and on behalf of the Victorian WorkCover Authority
A.C.N. 606 104 910
GPO Box 4695 MELBOURNE VIC 3001
Telephone (03) 7000 0700
Toll Free 1800 365 842 (1800 EML VIC)
Fax (03) 7000 0701

Compliance Pack

ENTERPRISE BARGAINING AGREEMENT

Modern awards cover a whole industry or occupation and provide a safety net of minimum pay rates and employment conditions.

Enterprise agreements can be tailored to meet the needs of particular enterprises. An agreement must leave an employee better off overall when compared to the relevant award or awards.

Enterprise agreements are collective agreements made at an enterprise level between employers and employees about terms and conditions of employment. Metcalf's EBA shows below: (Figure 12 and 13)

Figure 12

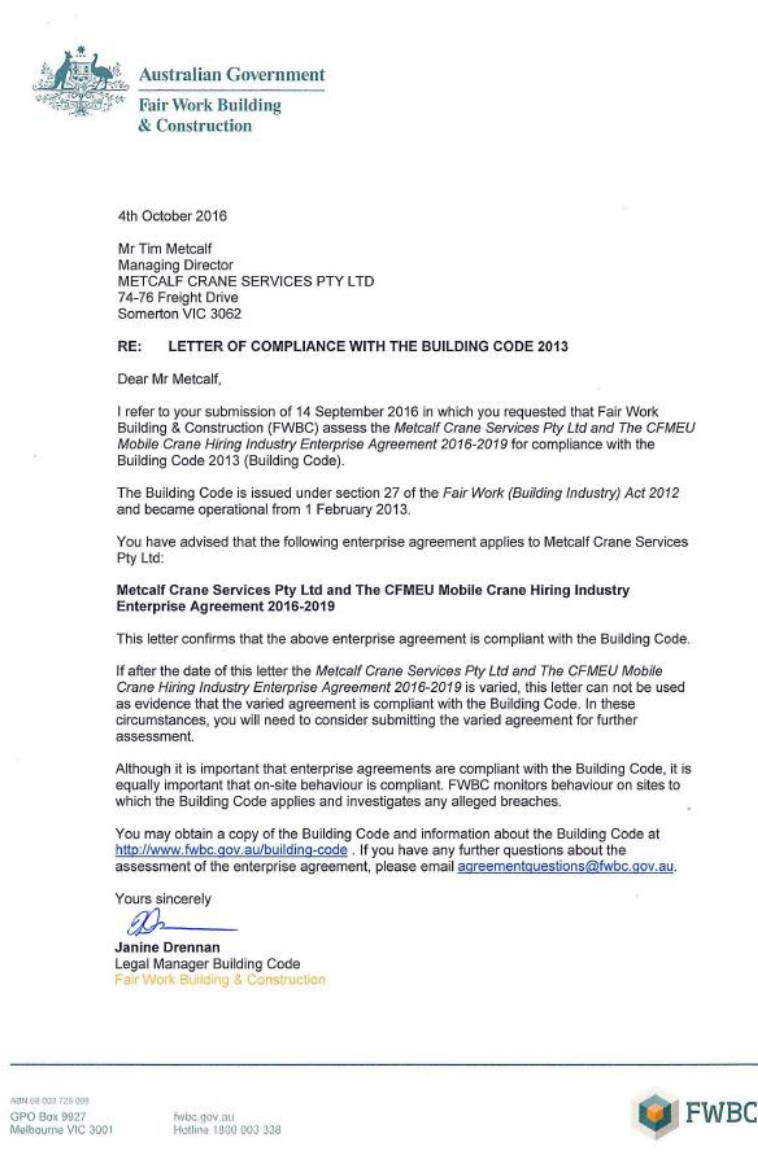


Figure 13



Australian Government
Australian Building and
Construction Commission

4 April 2018

Mr Paul Finnerty
General Manager
Metcalf Crane Services Pty Ltd
74 - 76 Freight Drive
SOMERTON VICTORIA 3062

DETERMINATION OF COMPLIANCE WITH SECTION 11
ABCC EA ID: EA5746
FWC Matter Number: AG2016/5531
FWC Variation Number: AG2017/5754

Dear Mr Finnerty,

On 4 April 2018 you requested advice from the Australian Building and Construction Commission (ABCC) on whether the registered enterprise agreement listed in your request meets the requirements of the *Code for the Tendering and Performance of Building Work 2016* (the Building Code 2016).

This Determination of Compliance is issued for the following registered enterprise agreement because it meets the requirements of section 11 of the Building Code 2016:

**METCALF CRANE SERVICES PTY LTD AND THE CFMEU MOBILE CRANE HIRING
INDUSTRY ENTERPRISE AGREEMENT 2016 - 2019**

Accordingly, by virtue of section 22(3) of the Building Code, this determination is taken to be conclusive of the fact that this registered enterprise agreement meets the requirements of section 11 of the Building Code 2016.

Note: This Determination of Compliance is based on the enterprise agreement registered with the Fair Work Commission at the date of this determination. If the registered enterprise agreement is varied after this date, the Determination of Compliance ceases to be effective. In these circumstances, you will need to consider submitting the varied agreement for further advice.

Parties must also comply with all relevant provisions of the Building Code 2016 in relation to their practical on-site application. The ABCC monitors behaviour on sites to which the Building Code applies and investigates any alleged breaches. The ABCC can be contacted through its hotline on 1800 003 338 or at www.abcc.gov.au.

The Building Code 2016 is available at <https://www.legislation.gov.au/Details/F2016L01859>.

Yours sincerely



Tom Cagorski
Legal Manager – Agreement Compliance
Australian Building and Construction Commission
